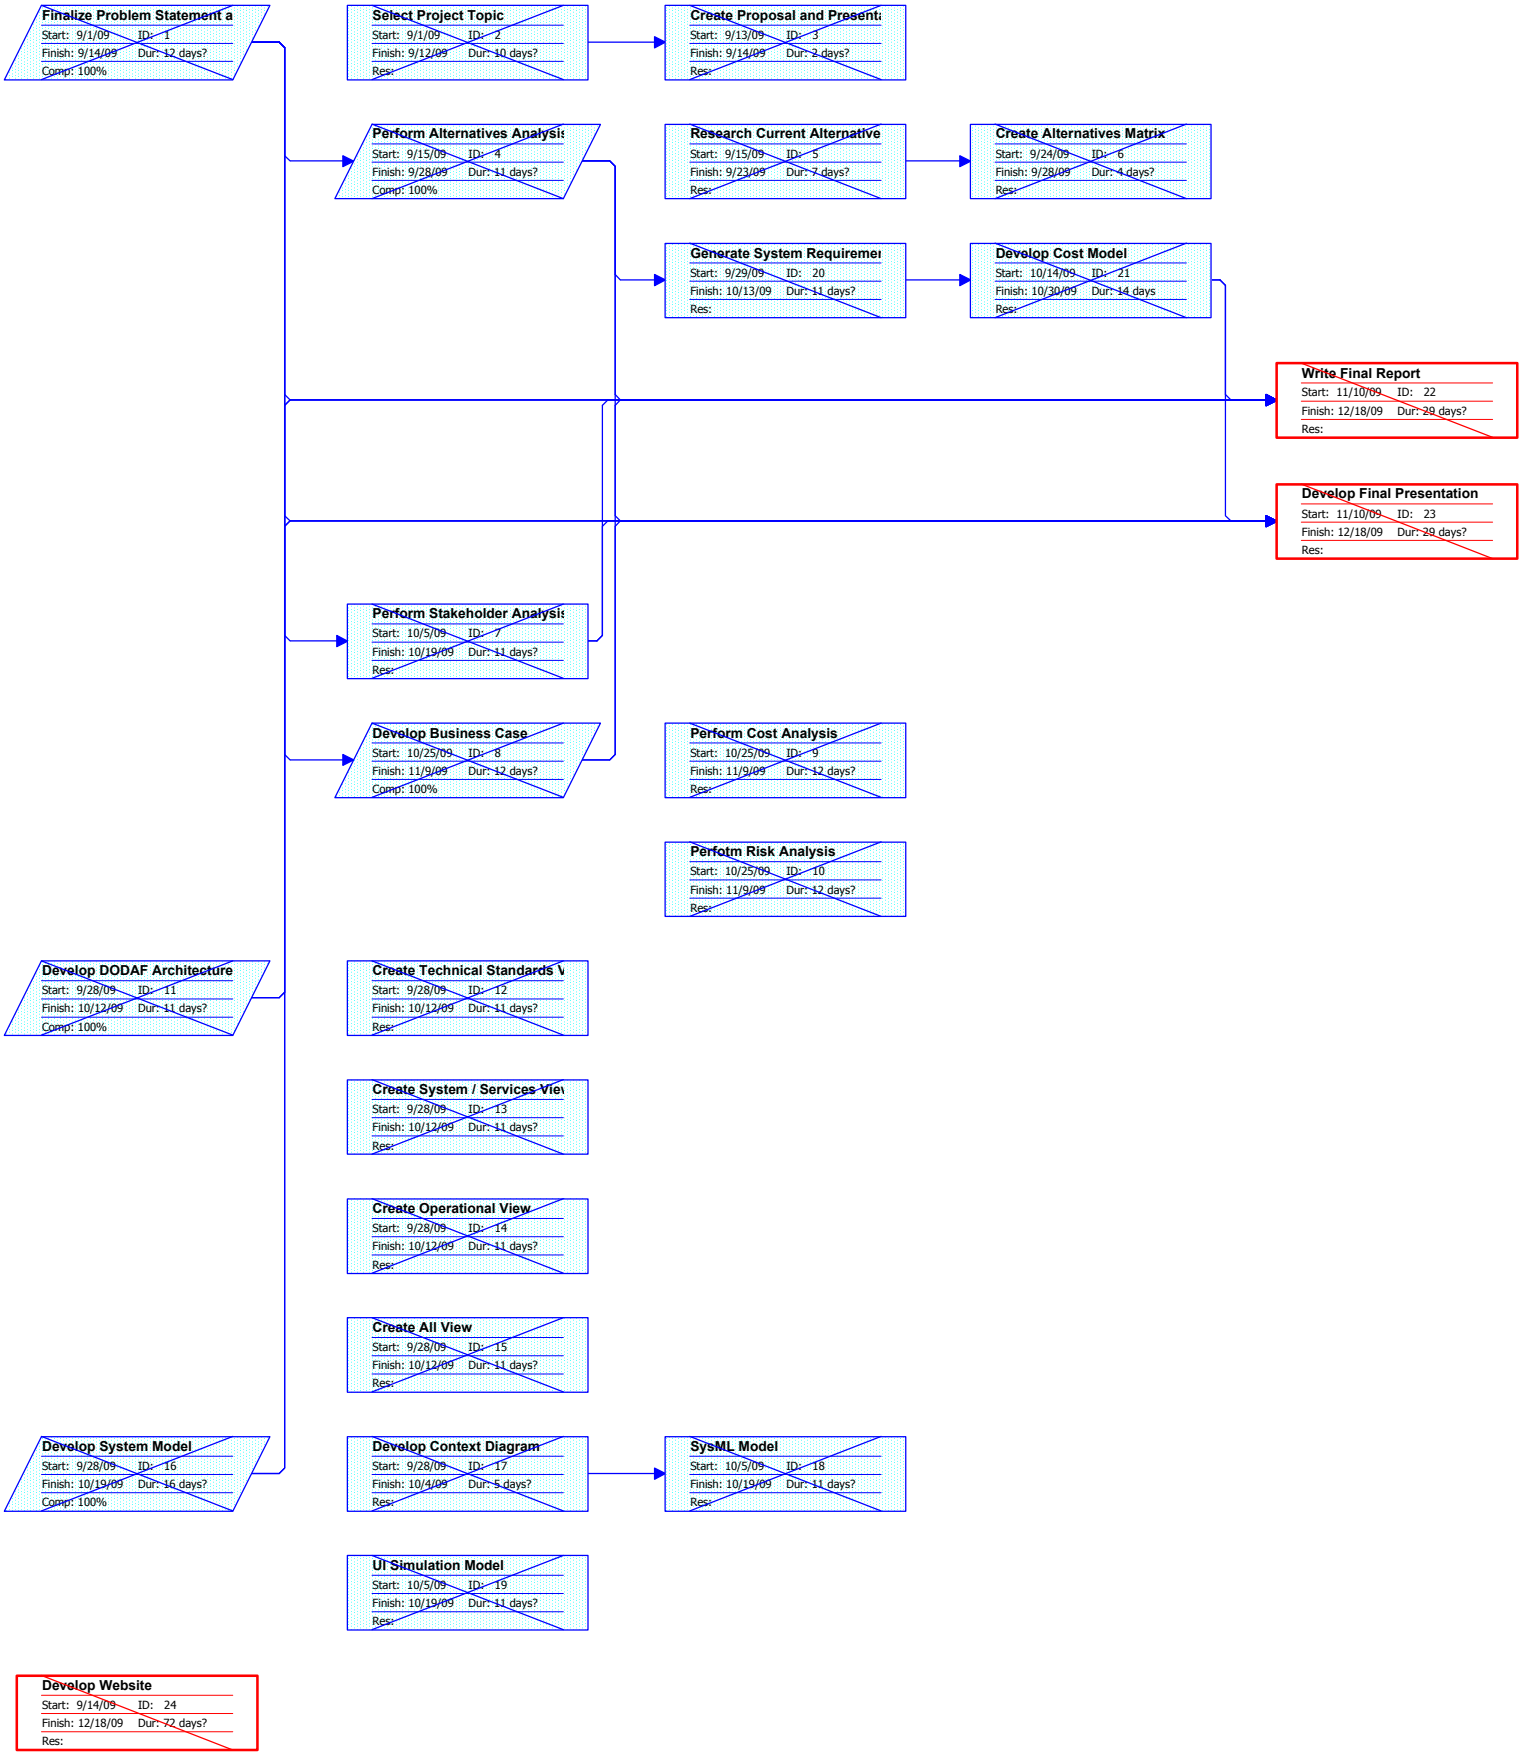
Finalize Problem Statement a
Start: 9/1/09 ID: 1
Finish: 9/14/09 Dur: 12 days?
Comp: 100%
Select Project Topic
Start: 9/1/09 ID: 2
Finish: 9/12/09 Dur: 10 days?
Res:
Create Proposal and Presenta
Start: 9/13/09 ID: 3
Finish: 9/14/09 Dur: 2 days?
Res:
Perform Alternatives Analysis
Start: 9/15/09 ID: 4
Finish: 9/28/09 Dur: 11 days?
Comp: 100%
Research Current Alternative
Start: 9/15/09 ID: 5
Finish: 9/23/09 Dur: 7 days?
Res:
Create Alternatives Matrix
Start: 9/24/09 ID: 6
Finish: 9/28/09 Dur: 4 days?
Res:
Generate System Requiremer
Start: 9/29/09 ID: 20
Finish: 10/13/09 Dur: 11 days?
Res:
Develop Cost Model
Start: 10/14/09 ID: 21
Finish: 10/30/09 Dur: 14 days
Res:
Write Final Report
Start: 11/10/09 ID: 22
Finish: 12/18/09 Dur: 29 days?
Res:
Develop Final Presentation
Start: 11/10/09 ID: 23
Finish: 12/18/09 Dur: 29 days?
Res:
Perform Stakeholder Analysis
Start: 10/5/09 ID: 7
Finish: 10/19/09 Dur: 11 days?
Res:
Develop Business Case
Start: 10/25/09 ID: 8
Finish: 11/9/09 Dur: 12 days?
Comp: 100%
Perform Cost Analysis
Start: 10/25/09 ID: 9
Finish: 11/9/09 Dur: 12 days?
Res:
Perfotm Risk Analysis
Start: 10/25/09 ID: 10
Finish: 11/9/09 Dur: 12 days?
Res:
Develop DODAF Architecture
Start: 9/28/09 ID: 11
Finish: 10/12/09 Dur: 11 days?
Comp: 100%
Create Technical Standards V
Start: 9/28/09 ID: 12
Finish: 10/12/09 Dur: 11 days?
Res:
Create System / Services Vie
Start: 9/28/09 ID: 13
Finish: 10/12/09 Dur: 11 days?
Res:
Create Operational View
Start: 9/28/09 ID: 14
Finish: 10/12/09 Dur: 11 days?
Res:
Create All View
Start: 9/28/09 ID: 15
Finish: 10/12/09 Dur: 11 days?
Res:
Develop System Model
Start: 9/28/09 ID: 16
Finish: 10/19/09 Dur: 16 days?
Comp: 100%
Develop Context Diagram
Start: 9/28/09 ID: 17
Finish: 10/4/09 Dur: 5 days?
Res:
SysML Model
Start: 10/5/09 ID: 18
Finish: 10/19/09 Dur: 11 days?
Res:
UI Simulation Model
Start: 10/5/09 ID: 19
Finish: 10/19/09 Dur: 11 days?
Res:
Develop Website
Start: 9/14/09 ID: 24
Finish: 12/18/09 Dur: 72 days?
Res:
